

LAB 2 REPORT

Agile Backlog Creation & Sprint Simulation in Jira

Scenario: Student Club Event Ticketing & Budget Portal

NAME:Snehitha

SRN:PES1UG24CS315

1. Objective

The objective of this lab is to use Jira to convert functional requirements from Lab 1 into Agile Epics and User Stories, prioritize and estimate the backlog, simulate two one-week sprints, and analyse progress using Jira's Burndown Chart.

2. Project Information


Item	Details
Project	Student club event ticketing and budget portal
Jira board key	SCETBP
Methodology	Agile Scrum
Management type	Company-managed
Scenario	Student Club Event Ticketing & Budget Portal
Actors	Club Lead, Campus Admin, Finance Officer, Attendee

3. Epics

The Lab 1 functional requirements were grouped into three major functional themes.

Epic	Description
Epic1-Event Proposal Management	Manage submission, review, approval/rejection, and status tracking of student club event proposals.
Epic2-Budget Allocation Management	Manage university budget allocation requests, finance review, approval/rejection, and status tracking.
Epic3-QR Ticket & Check-in Management	Generate QR tickets for approved events and validate tickets during attendee check-in.

Jira Backlog with Epics and User Stories

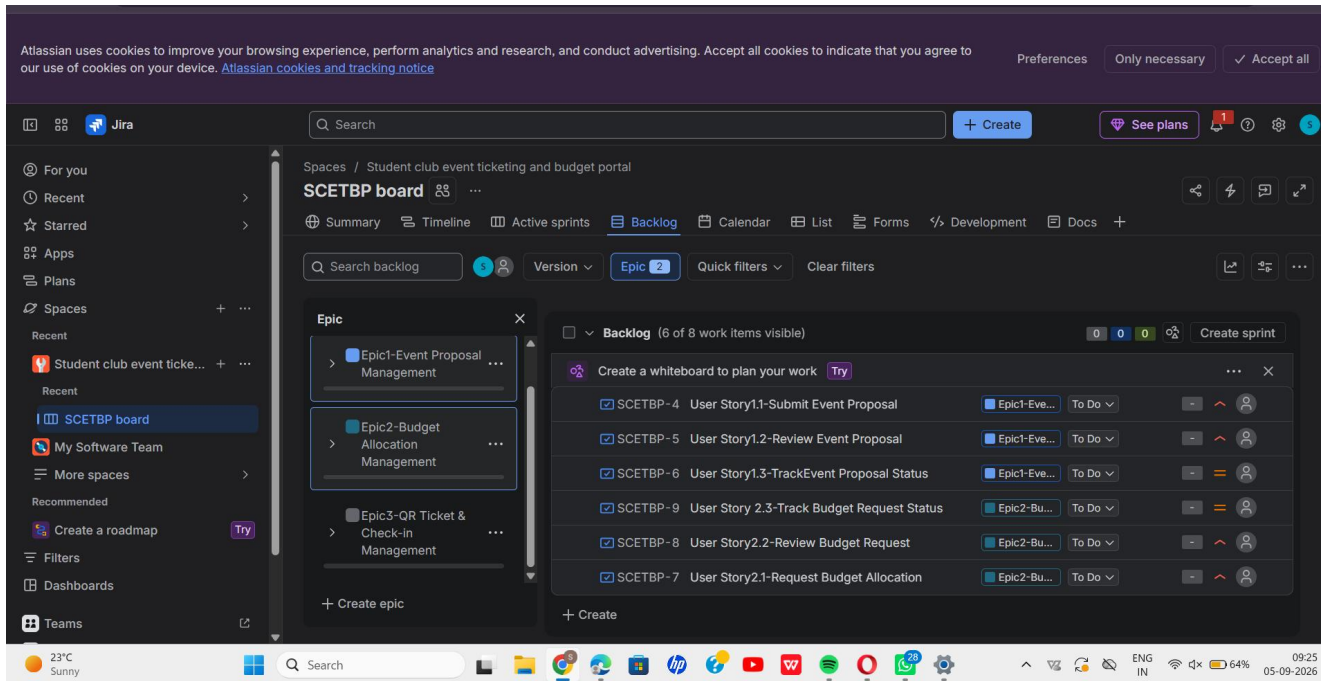

SCETBP-4	User Story1.1-Submit Event Proposal	Epic1-Event Propo...	To Do	-	^	👤
SCETBP-5	User Story1.2-Review Event Proposal	Epic1-Event Propo...	To Do	-	^	👤
SCETBP-6	User Story1.3-TrackEvent Proposal Status	Epic1-Event Propo...	To Do	-	=	👤
SCETBP-11	User Story 3.2-Check-in & Validate QR Ticket	Epic3-QR Ticket & ...	To Do	-	^	👤
SCETBP-10	User Story3.1-Generate QR Ticket	Epic3-QR Ticket & ...	To Do	-	^	👤
SCETBP-9	User Story 2.3-Track Budget Request Status	Epic2-Budget Allo...	To Do	-	=	👤
SCETBP-8	User Story2.2-Review Budget Request	Epic2-Budget Allo...	To Do	-	^	👤
SCETBP-7	User Story2.1-Request Budget Allocation	Epic2-Budget Allo...	To Do	-	^	👤

4. User Stories

Key	Story	Epic	Role	User Story	Priority	Points
SCETBP-4	User Story1.1-Submit Event Proposal	Epic1	Club Lead	As a Club Lead, I want to submit an event proposal containing the event name, date, venue, description, and expected attendance, so that the university can review my proposed event.	High	5
SCETBP-5	User Story1.2-Review Event Proposal	Epic1	Campus Admin	As a Campus Admin, I want to review an event proposal and approve or reject it, so that only authorized student club events can proceed.	High	3
SCETBP-6	User Story1.3-Track Event Proposal Status	Epic1	Club Lead	As a Club Lead, I want to view the status of my submitted event proposal, so that I know whether my proposal is pending, approved, or rejected.	Medium	3
SCETBP-7	User Story2.1-Request Budget Allocation	Epic2	Club Lead	As a Club Lead, I want to submit a budget allocation request with the requested amount and required budget details, so that I can request university funding for my event.	High	5
SCETBP-8	User Story2.2-Review Budget Request	Epic2	Finance Officer	As a Finance Officer, I want to review a budget	High	5


				allocation request and approve or reject it, so that university funds are allocated through the approved workflow.		
SCETBP-9	User Story2.3-Track Budget Request Status	Epic2	Club Lead	As a Club Lead, I want to view the status of my budget request, so that I know whether my funding request has been approved or rejected.	Medium	3
SCETBP-10	User Story3.1-Generate QR Ticket	Epic3	Attendee	As an Attendee, I want to receive a unique QR-code ticket linked to an approved event and my attendee record, so that I can use the ticket for event entry.	High	5
SCETBP-11	User Story3.2-Check-in & Validate QR Ticket	Epic3	Campus Admin	As a Campus Admin, I want to check in an attendee by validating their QR-code ticket, so that only valid tickets linked to the event are accepted and the attendee's entry is recorded.	High	5

5. Prioritization and Story Point Estimation

Priorities were assigned as High or Medium according to user impact and the importance of the functionality to the portal workflow. Story Points were assigned using a Fibonacci-style relative estimation scale, considering complexity, effort, risk, and uncertainty.

Total backlog estimate: 34 Story Points.

Story Point Assignments and Priorities

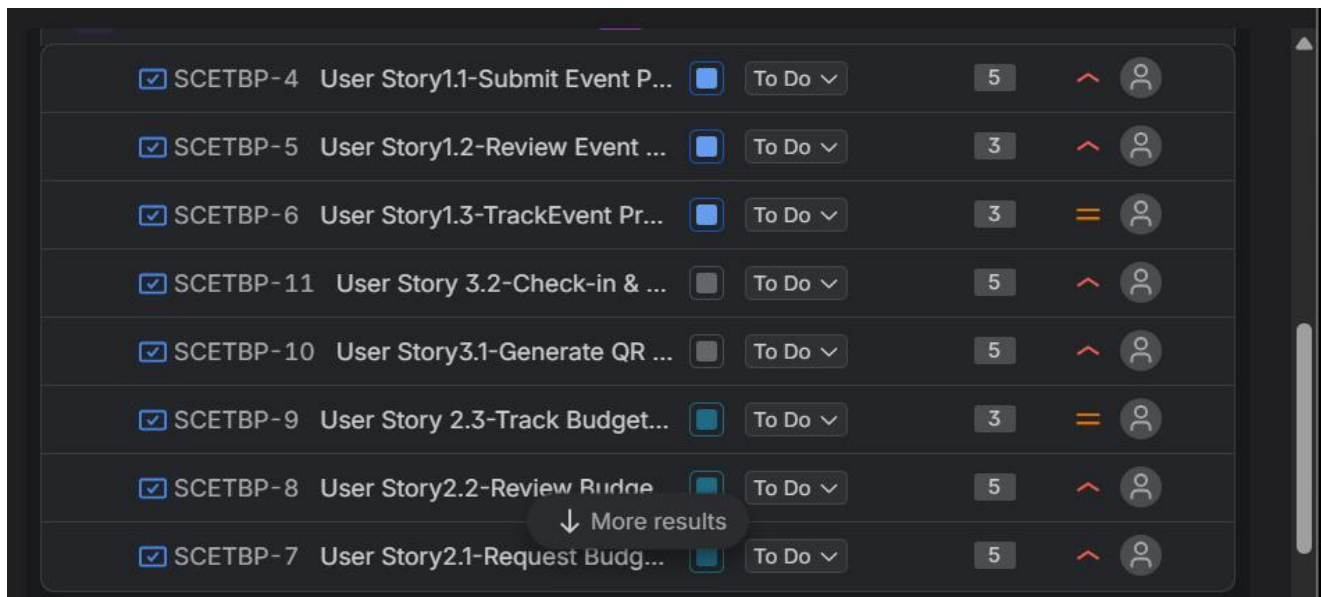

6. Sprint 1

Sprint 1 was planned as a one-week sprint with the goal: "Implement core event proposal, budget allocation, and QR ticket functionality."



Issue	Story	Points
SCETBP-4	Submit Event Proposal	5
SCETBP-7	Request Budget Allocation	5
SCETBP-5	Review Event Proposal	3
SCETBP-8	Review Budget Request	5
SCETBP-10	Generate QR Ticket	5
TOTAL		23


The selected stories were moved through To Do → In Progress → Done to simulate sprint progress. All five Sprint 1 stories were completed, leaving 0 Story Points remaining.

Sprint 1 – Active Sprint / Completed Sprint Board

The screenshot displays the Jira interface for the 'SCETBP board'. The board is organized into three columns: 'TO DO', 'IN PROGRESS', and 'DONE'. The 'TO DO' column contains five user stories, each with a sub-task and a point value. The 'IN PROGRESS' and 'DONE' columns are currently empty.

Column	User Story	Sub-task	Points
TO DO	User Story1-Submit Event Proposal	Epic1-Event Proposal Management	5
	User Story2.1-Request Budget Allocation	Epic2-Budget Allocation Management	5
	User Story1.2-Review Event Proposal	Epic1-Event Proposal Management	3
	User Story2.2-Review Budget Request	Epic2-Budget Allocation Management	5
	User Story3.1-Generate QR Ticket	Epic3-QR Ticket & Check-in Management	5
IN PROGRESS			
DONE			

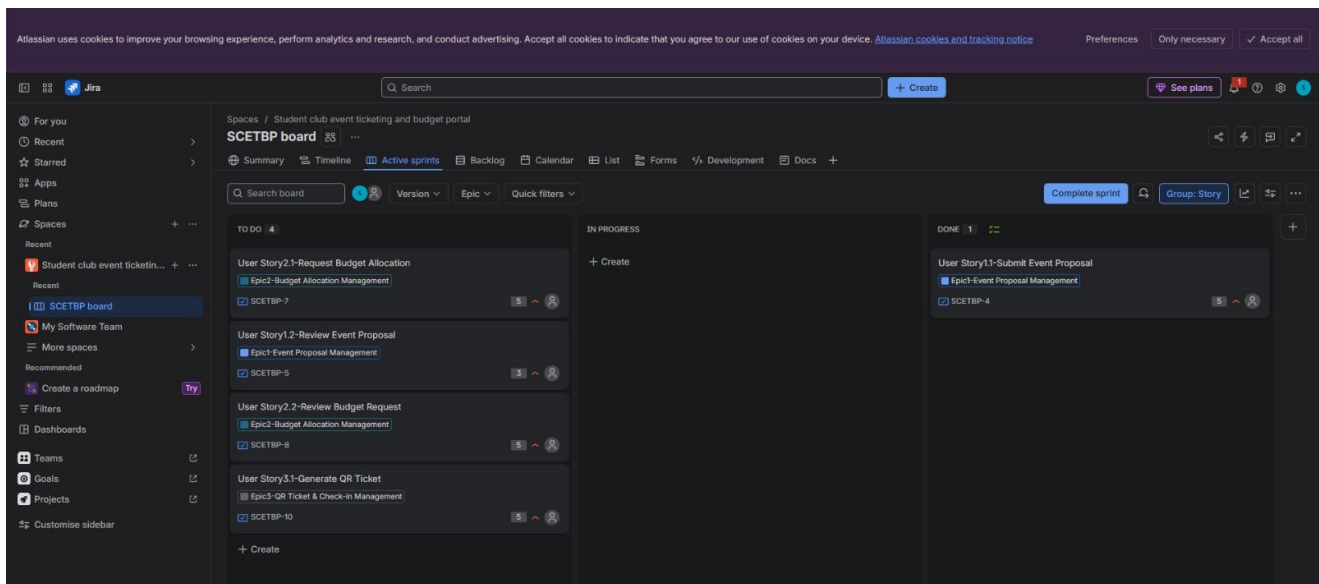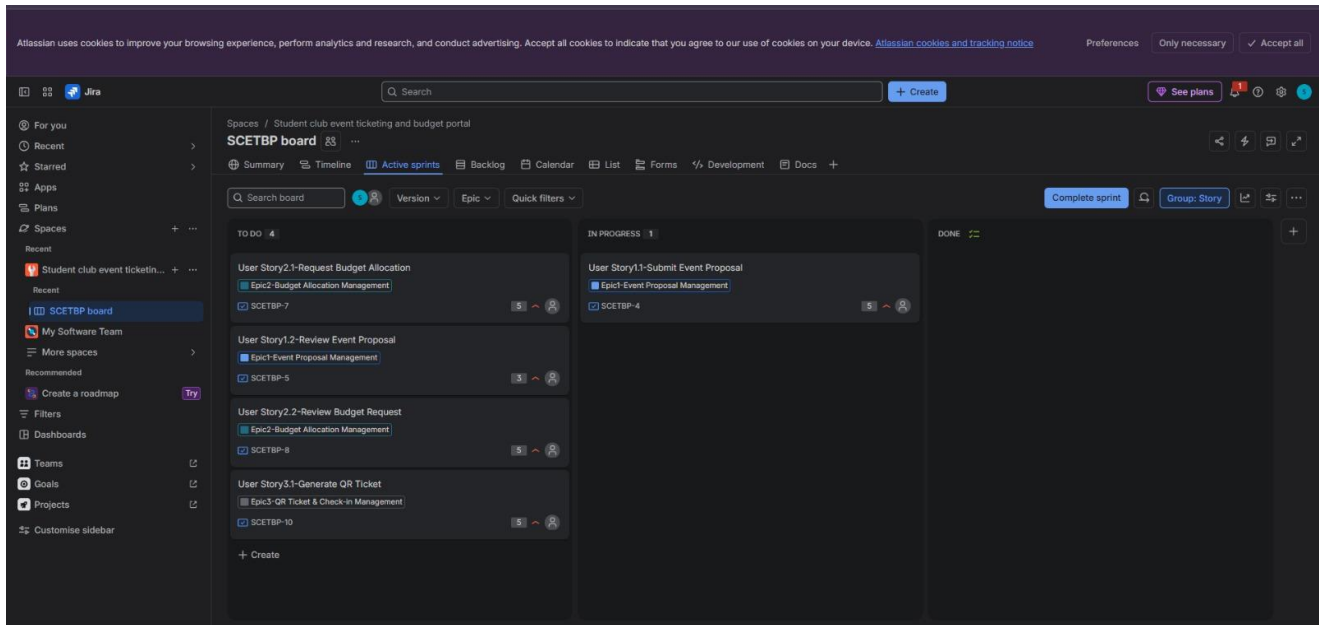

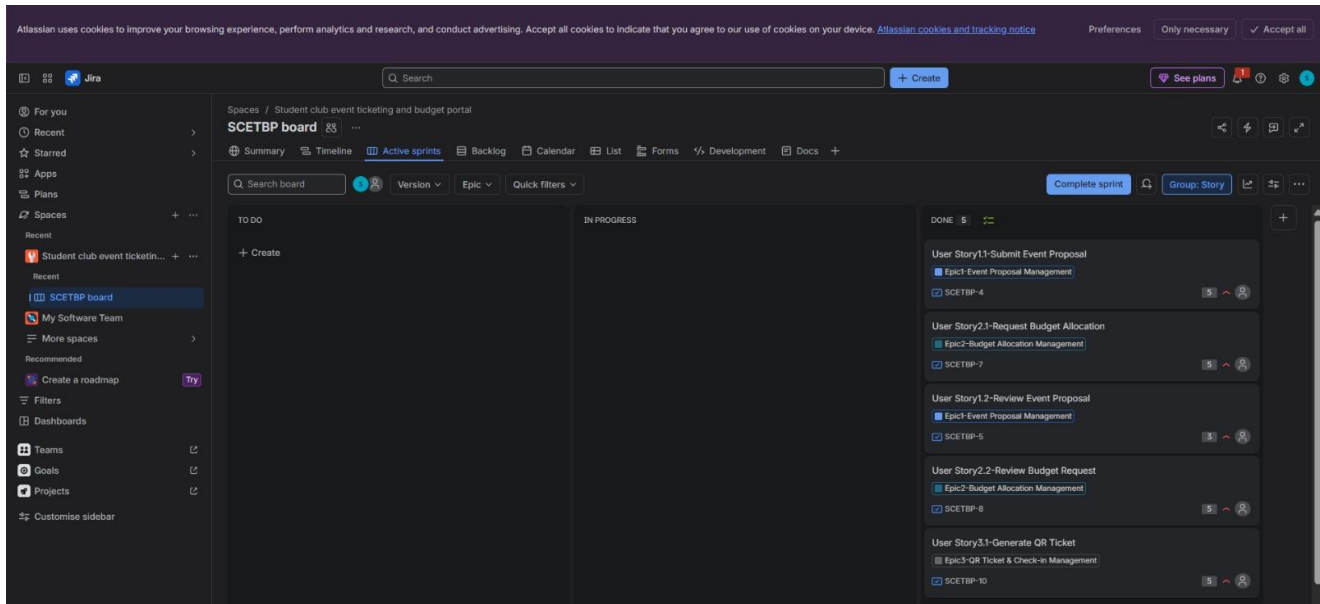


7. Sprint 2


Sprint 2 was created from the remaining backlog items. It was also planned as a one-week sprint.

Issue	Story	Points
SCETBP-6	Track Event Proposal Status	3
SCETBP-9	Track Budget Request Status	3
SCETBP-11	Check-in & Validate QR Ticket	5
TOTAL		11

Sprint 2 goal: "Complete event and budget status tracking and QR ticket validation." All three Sprint 2 stories were completed, leaving 0 Story Points remaining.

Sprint 2 – Active Sprint / Completed Sprint Board

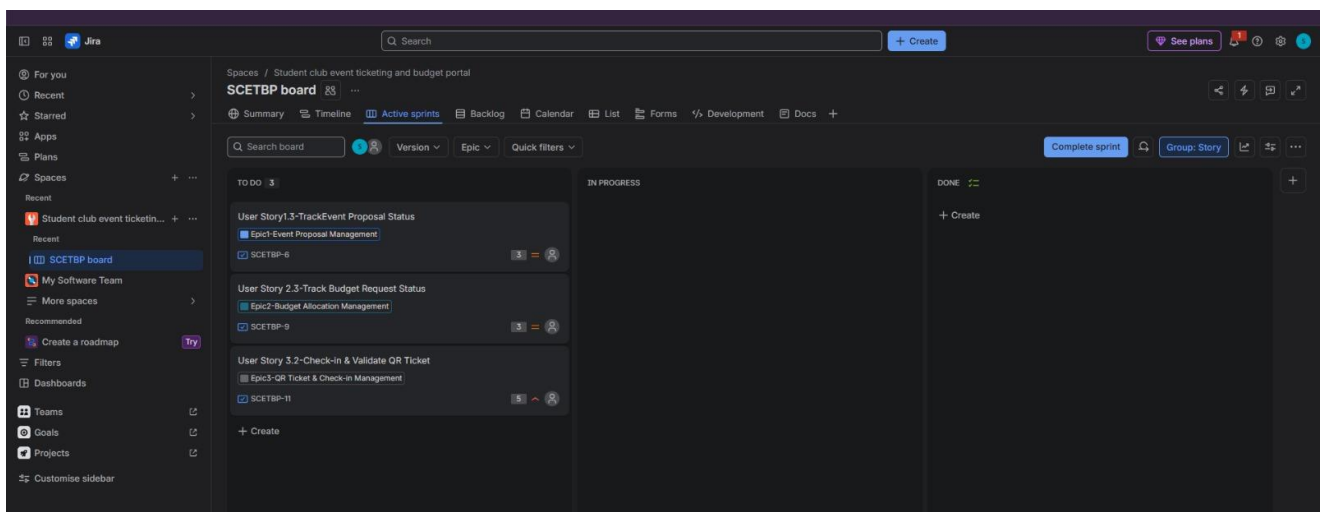


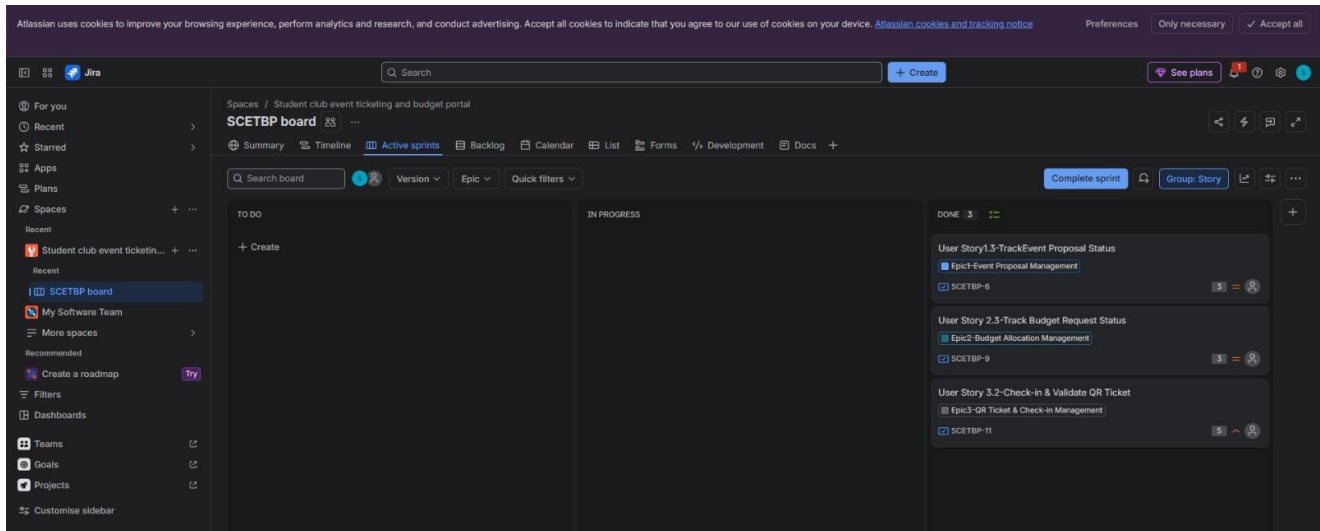

8. Burndown Chart – Sprint 1

The Sprint 1 Burndown Chart was viewed using Story Points as the estimation statistic. The sprint started with 23 points and recorded completion of all five stories, reducing the remaining work to 0.


Burndown Chart – Sprint 1

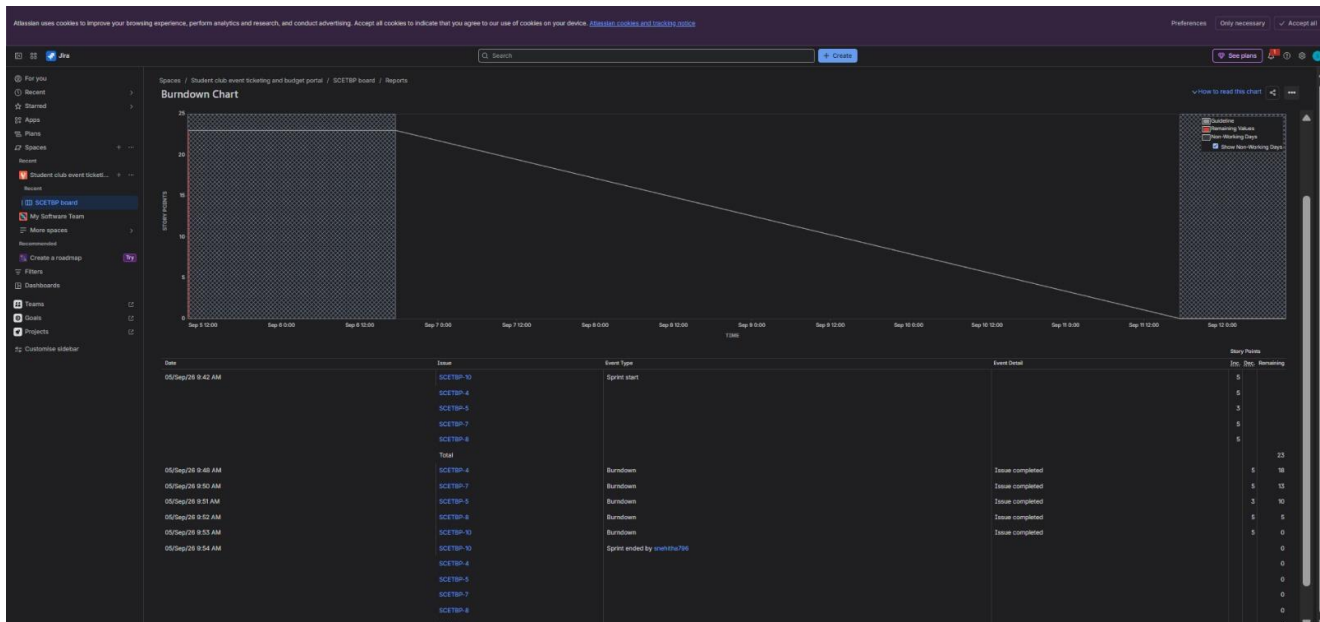

9. Burndown Chart – Sprint 2

The Sprint 2 Burndown Chart was viewed using Story Points as the estimation statistic. The sprint started with 11 points and all three stories were completed, reducing the remaining work to 0.

Burndown Chart – Sprint 2

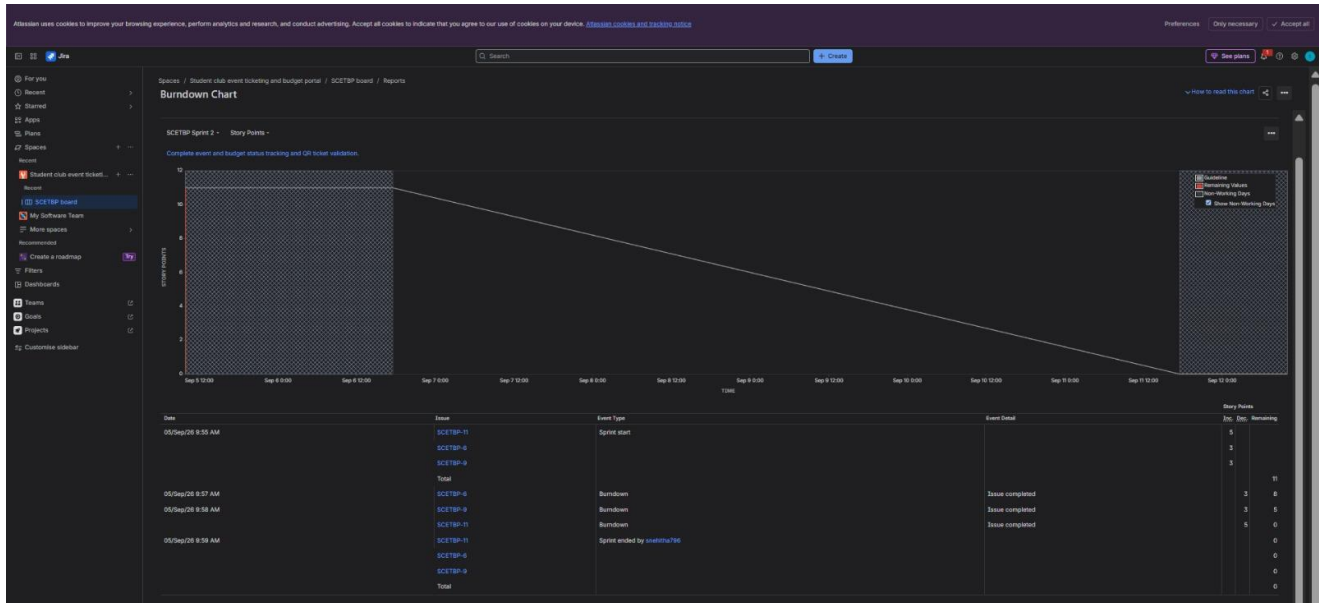

§The following answers are based on the actual simulated Jira work completed in this lab.

1. Did your estimations reflect the actual effort?

The estimations were reasonably aligned with the simulated effort. The larger stories were assigned 5 points, while smaller status-tracking/review stories were assigned 3 points. Since this was a short simulation rather than a real implementation, the points mainly represented relative complexity and uncertainty rather than measured development time.

2. Was your backlog well-prioritized?

Yes. Core workflow functionality was given High priority: submitting and reviewing event proposals, requesting and reviewing budgets, generating QR tickets, and validating QR tickets. Status-tracking stories were given Medium priority because they support visibility after the main workflows are established.

3. How did your simulated sprint align with your plan?

The sprint plan was followed successfully. Sprint 1 contained 23 Story Points covering the core event, budget, and QR-ticket functionality, and all selected stories were completed. Sprint 2 contained the remaining 11 Story Points for status tracking and QR validation, and those stories were also completed.

4. What insights did the burndown chart give about your team's capacity?

The burndown charts showed that the planned work was completed and the remaining Story Points reached zero within each sprint. The sharp drops occurred because the lab was a rapid simulation in which stories were moved to Done close together in time. In a real project, a similarly sharp drop could indicate that work was completed late or that estimation/task breakdown should be reviewed. The exercise also showed that the team's simulated capacity was sufficient for 23 points in Sprint 1 and 11 points in Sprint 2.
